DMLL and Associated Library Works

ID	Task Name	Duration	Start
1			
2	Completion of data survey	0 wks	Fri 21/03/14
3	Finalise layout and agree budget	3 wks	Mon 10/03/14
4	Approval to proceed	1 wk	Mon 31/03/14
5	Detailed design	4 wks	Mon 07/04/14
6	Prepare tender documents	2 wks	Mon 05/05/14
7	Out to tender	0 wks	Mon 19/05/14
8	**BOOK MOVE**	1 wk	Mon 19/05/14
9	Tender period	4 wks	Mon 19/05/14
10	Tenders returned	0 wks	Fri 13/06/14
11	Review and recommend	1 wk	Mon 16/06/14
12	Place order	0 wks	Mon 23/06/14
13	Contractor mobilsation	4 wks	Mon 23/06/14
14	**CLEAR 3RD FLOOR**	2 wks	Mon 07/07/14
15	Start on site	0 wks	Mon 21/07/14
16	Contract period	8 wks	Mon 21/07/14
17	Practical Completion	0 wks	Fri 12/09/14
18	Client fit-out	1 wk	Mon 15/09/14
19	**OPERATIONAL DATE**	**0 wks**	**Mon 22/09/14**

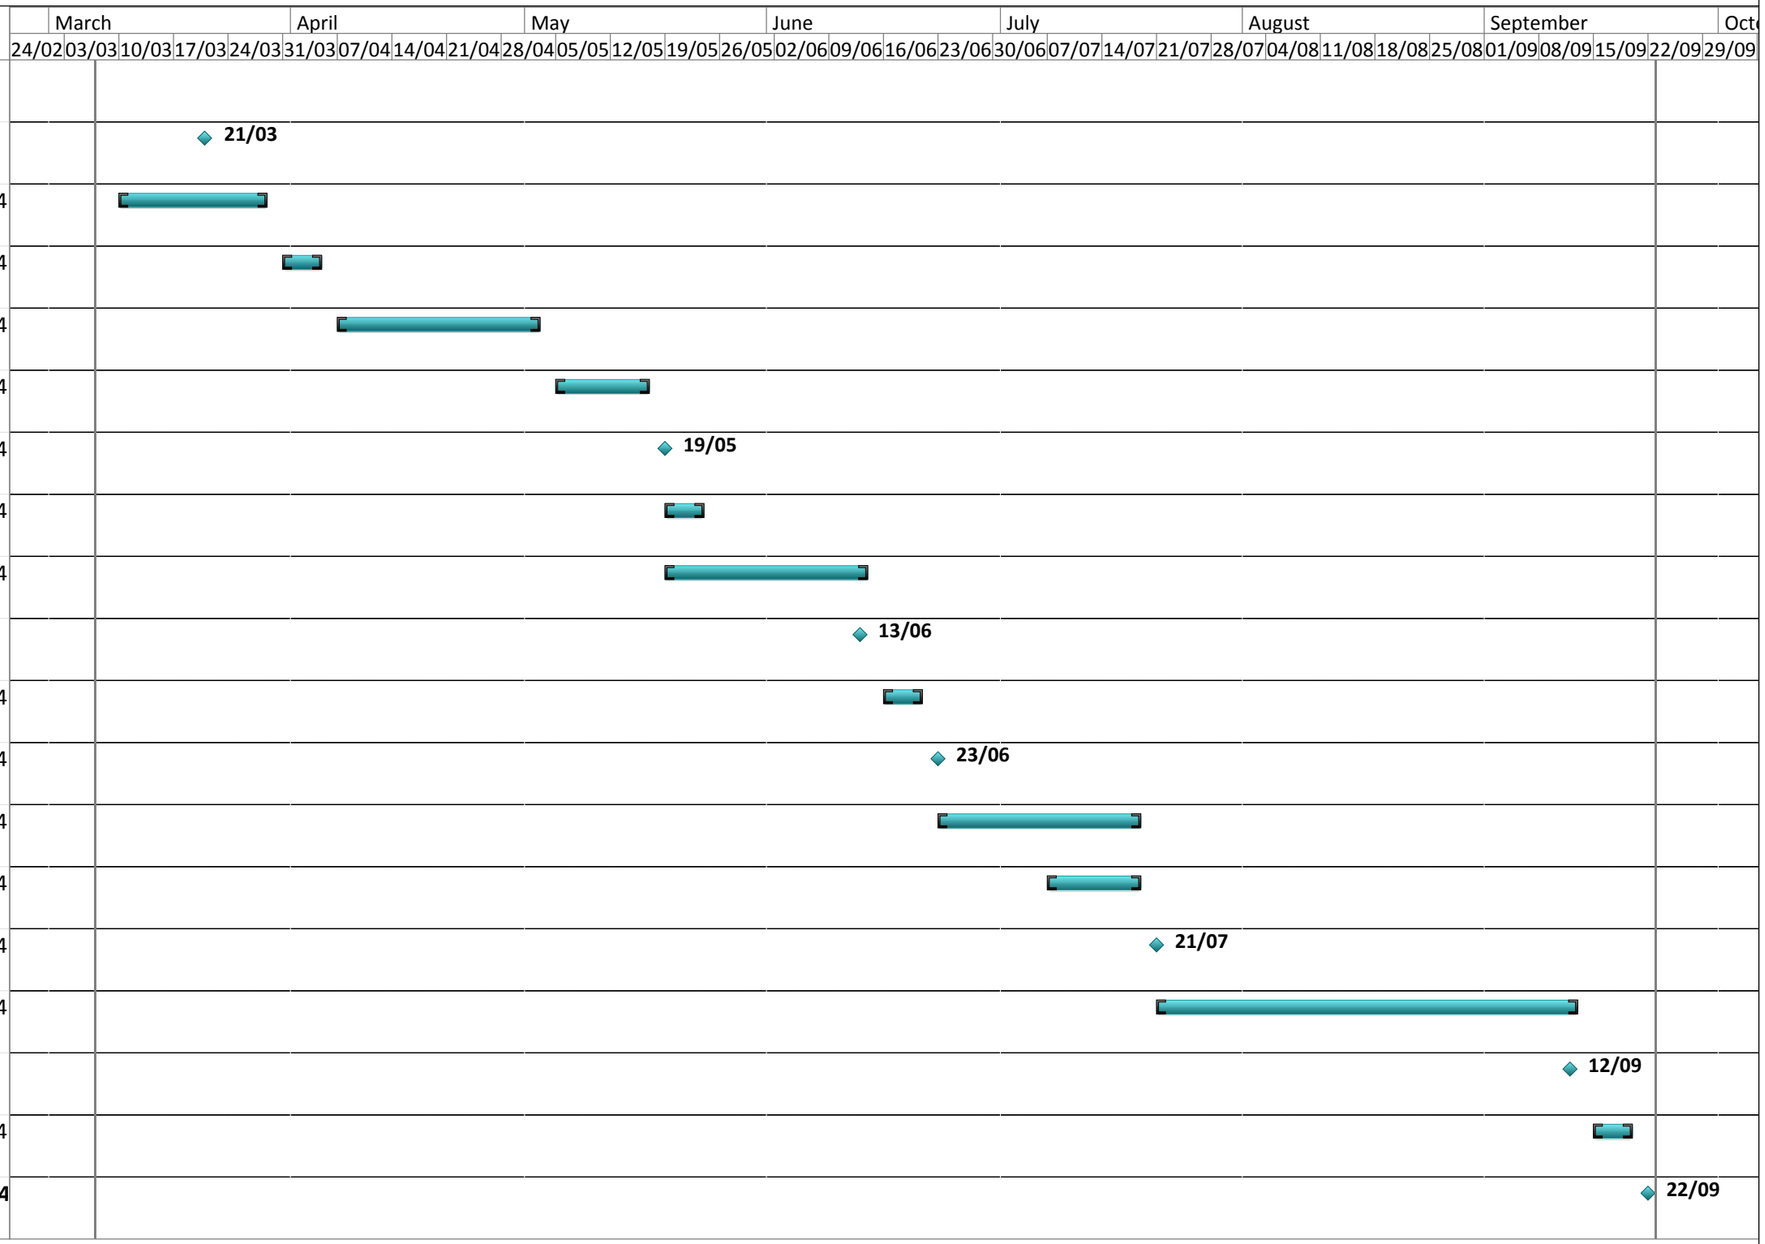

DMLL & associated Library Works
PRELIMINARY PROGRAMME
7 March 2014

Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline
Split	External Tasks	Inactive Summary	Manual Summary	Progress
Milestone	External Milestone	Manual Task	Start-only	
Summary	Inactive Task	Duration-only	Finish-only	
